

It's real.

Memorandum

To: Mayor and City Council Members
Steve Parker, City Manager

From: Melissa Reynolds, P.E., MPA, CFM, City Engineer

Through: Rick Cortes, Deputy City Manager

Subject: Resolution of the City Council of the City of Seguin, Texas authorizing the City Manager to execute Change Order No. 6 with D&D Contractors, Inc. for the North Heideke Street Drainage Improvement Project (a GLO CDBG-MIT Grant Project) for a decrease of \$593,023.46; and declaring an effective date.


Date: January 6, 2026

Historical Background

The City of Seguin was awarded a grant from the General Land Office for flood mitigation and infrastructure improvements in the amount of \$37,891,885.50. This grant is for construction of drainage improvements in the following four areas:

Walnut Branch
Mays Creek
North Heideke
North Guadalupe

In December 2021, City Council awarded project related engineering services to TRC Companies, Inc. On December 17, 2024, the construction contract was awarded to D&D Contractors, Inc. in the amount of \$17,911,808.79. On August 19th, City Council authorized Change Order Nos. 1, 2, and 3. On October 4th, City Council authorized Change Order No. 4. On November 11th, City Council authorized Change Order No. 5.

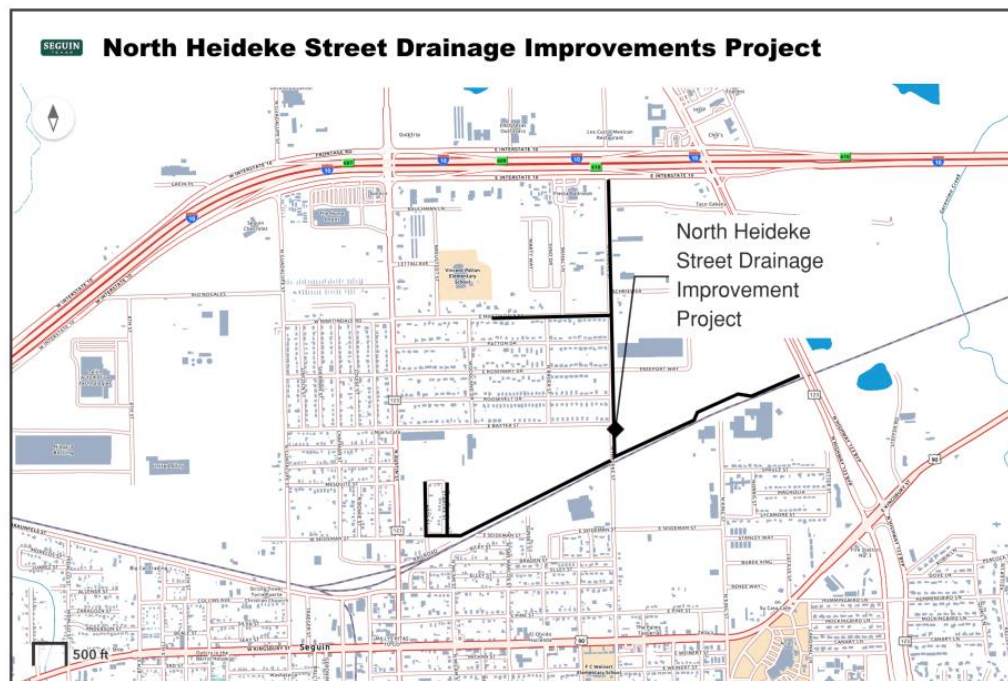

Original Contract \$ 17,911,808.79

Change Order	Impact	Cumulative Cost
		\$
1	\$ 25,810.69	17,937,619.48
		\$
2	\$ 2,447.23	17,940,066.71
		\$
3	\$ 3,031.22	17,943,097.93
		\$
4	\$ (2,683.57)	17,940,414.36
		\$
5	\$ (2,673.10)	17,937,741.26
		\$
6	\$ (593,023.46)	17,344,717.80
TOTAL	\$ (567,090.99)	

Action Requested

A change order has been requested to memorialize Change Order No. 6 additional shoring, concrete work, reinforced concrete pipe, and utility relocation necessitated by the stormwater improvements and a deduction of jack and bore items. The contract price will be decreased with Change Order No. 6 to \$17,344,717.80.

Procurement Methodology & Funding Source

This project originally went through the formal bidding process under bid number AF-2025-17. Funding for this change order has been secured through bonds and GLO CDBG-MIT grants

Staff Recommendation

Staff recommends the approval of this change order.

ATTACHMENTS

1. 2026-01-06 Resolution GLO Heideke CO
2. Change Order No. 6
